ISYS 1108 / 3474 Software Engineering Project Management

Week 6: Workshop

Dr Maria Spichkova

Senior Lecturer in Software Engineering

What's next...

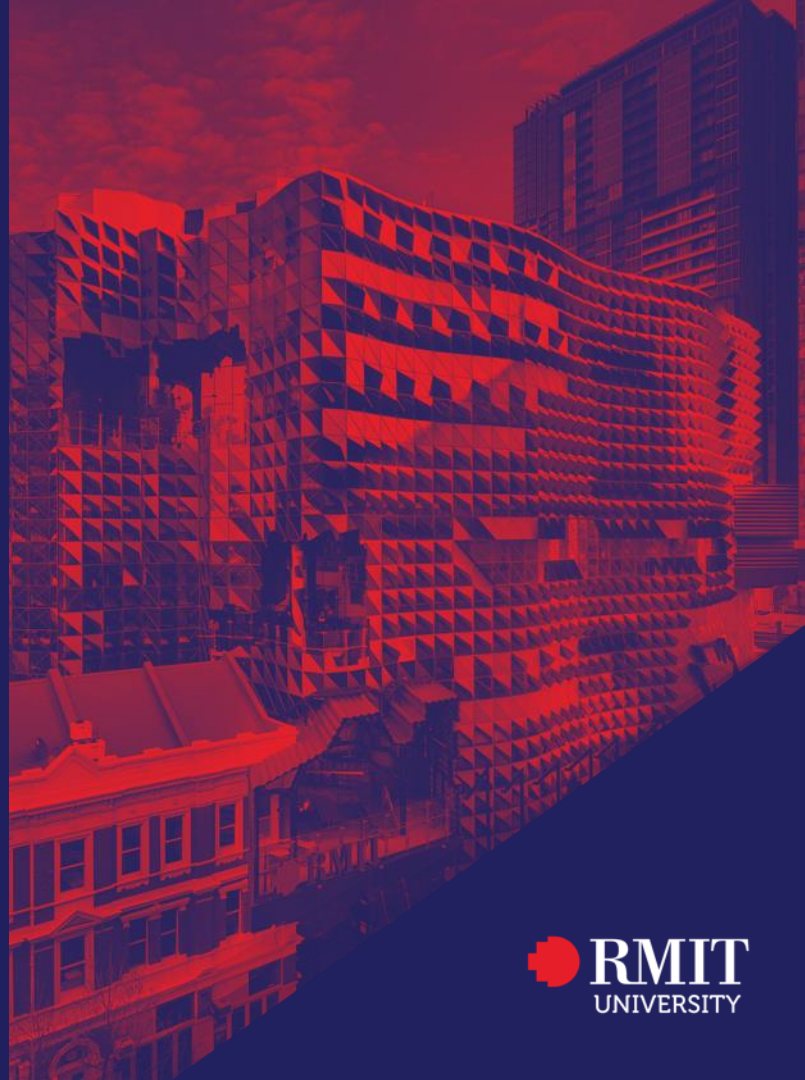

RMIT UNIVERSITY

Acknowledgement of Country

RMIT University acknowledges the people of the Woi wurrung and Boon wurrung language groups of the eastern Kulin Nation on whose unceded lands we conduct the business of the University.

RMIT University respectfully acknowledges their Ancestors and Elders, past and present.

RMIT also acknowledges the Traditional Custodians and their Ancestors of the lands and waters across Australia where we conduct our business.

Our plan for this session

- 😊 Agile estimates in story points
- 😊 Trello board
- 😊 Jira Board
- 😊 Team-based Assignment: Discussion

You will need to create Trello or Jira board in your Team-based assignment.

Reminder: Please check the marking criteria for A2 (below you can see the first 2 criteria)

Criteria	Ratings				Pts
Trello/Jira board layout	**3 pts** **Full marks** The board has correct format/layout as expected for Trello/Jira approach, including the presentation on PBI IDs, using labels, etc.	**2 pts** **Good** There are some mistakes, but the solution is generally reasonable. See feedback from the marker.	**1 pts** **Needs improvement** The solution contains many critical mistakes. See feedback from the marker.	**0 pts** **No marks** No link to the board submitted, or the board is completely incorrect, or you haven't contributed to the creation of this artefact.	3 pts
Completeness of the product backlog	**3 pts** **Full Marks** The set of cards presenting all PBIs (all cards on the boards) covers all functionalities requested by the client, none of the PBIs is out of scope, all items are correctly sorted by priorities. The spreadsheet version of the product backlog matches the board.	**2 pts** **Good** There are some mistakes, but the solution is generally reasonable. See feedback from the marker.	**1 pts** **Needs improvement** The solution contains many critical mistakes or the spreadsheet-version of the product backlog is missing. See feedback from the marker.	**0 pts** **Incorrect** No link to the board submitted, or the product backlog is completely incorrect/missing, or you haven't contributed to the creation of the product backlog.	3 pts

Activity 1: Agile estimates – Efforts in story points

Let's answer the following questions of the checklist and discuss required changes: Are the Efforts reasonable wrt. the PBIs?

Duration: approx. 10 minutes

PRODUCT BACKLOG

DoD1:
- Unit tests passed (code coverage 85%)
- Code peer reviewed
- Functional test based on ACs passed
- Regression testing completed
- Usability testing completed on Google Chrome (version 89) and Safari (version 14)
- Approved by the Product Owner

ID	ITEM	OWNER	PRIORITY	EFFORT in story points	STATUS	DEFINITION OF DONE
8	As a customer user, I want to update my payment method, so that my payment details are up-to-date.	Product Owner	High	2	To Do	DoD1
5	As a new franchisee user, I want to create a franchisee account, so that I can start working with Victoria Farms	Product Owner	Medium	8	To Do	DoD1
6	As a franchisee user, I want to update the contact details in my account, so that my customers can contact me	Product Owner	Medium	2	To Do	DoD1
7	As a customer user, I want to update the type of my order, so that the deliverer knows whether the order is urgent.	Product Owner	Low	2	To Do	DoD1

What about other (below) variants of effort allocation?

1	1	1
5	5	3
1	1	1
1	0.5	0.5

Activity 2: Product backlog – PBI Efforts

Duration: approx. 10 minutes

Open the document we discussed in Week 4 Workshop ***SEPM_Week_4_PB_WithMistakes.pdf*** *in Modules → Week 4 - Lectorials and Workshops*

Let's answer the following questions of the checklist and discuss required changes:

- Are the Efforts reasonable wrt. the PBIs?
- Is the syntax of efforts correct (Fibonacci numbers are used)?

Activity 3: Trello board – general structure (columns)

Duration: approx. 10 minutes

Let's create now a general structure (columns) of a Trello board for Scrum: Go to https://trello.com/home, register and start working with a board.

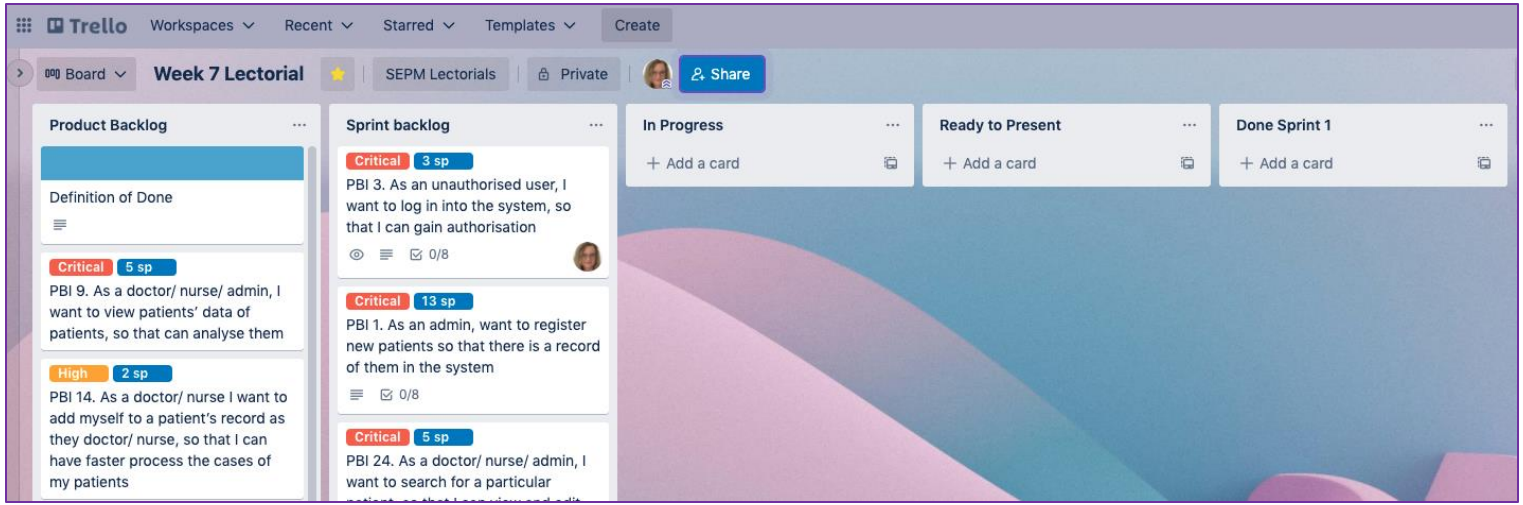

Scrum using Trello = Scrum + Kanban

Use one board only!

Columns

- Product backlog – or – Project backlog
- Sprint Backlog
- In progress
- Ready to present
- Done – or – Sprint 1 Done, Sprint 2 Done, ….

Cards

- Should be allocated, when ”In progress”
- Labels might be useful

Checklists

- Design, Implementation, Testing (or several items for several types of testing), Deployment, …
- Can be used to reflect DoD

Note: We shared with you a number of videos as additional hints (Week 6 - Lectorials and Workshops):

- Using Trello in Scrum: approx. 4 minutes
- How to create Trello board: approx. 6 minutes
- User Story Cards in Trello: approx. 9 minutes

Trello: Extra videos/ reading materials

We shared with you in the Canvas module for this week (Week 6 - Lectorials and Workshops) additional learning material (videos) to help you with today's activities:

- Using Trello in Scrum (approx. 4 minutes)
- How to create Trello board (approx. 6 minutes)
- User Story Cards in Trello (approx. 9 minutes)

Activity 4: Jira board – general structure (Scrum project)

Duration: approx. 20 minutes

Let's discuss now how to create a Scrum project in Jira.

Go to https://www.atlassian.com/software/jira, register and start working with the tool: Create a Scrum project

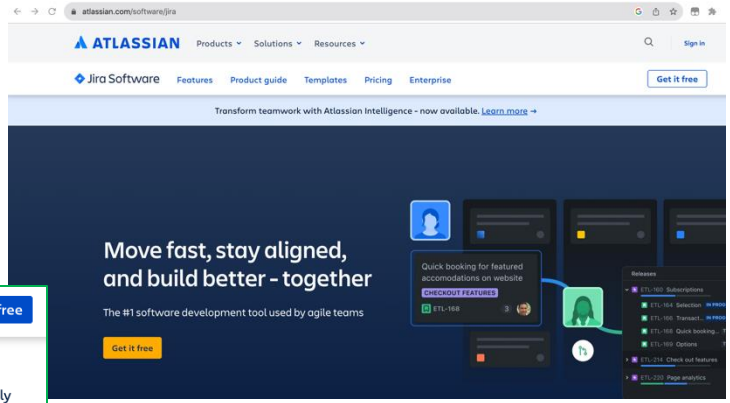

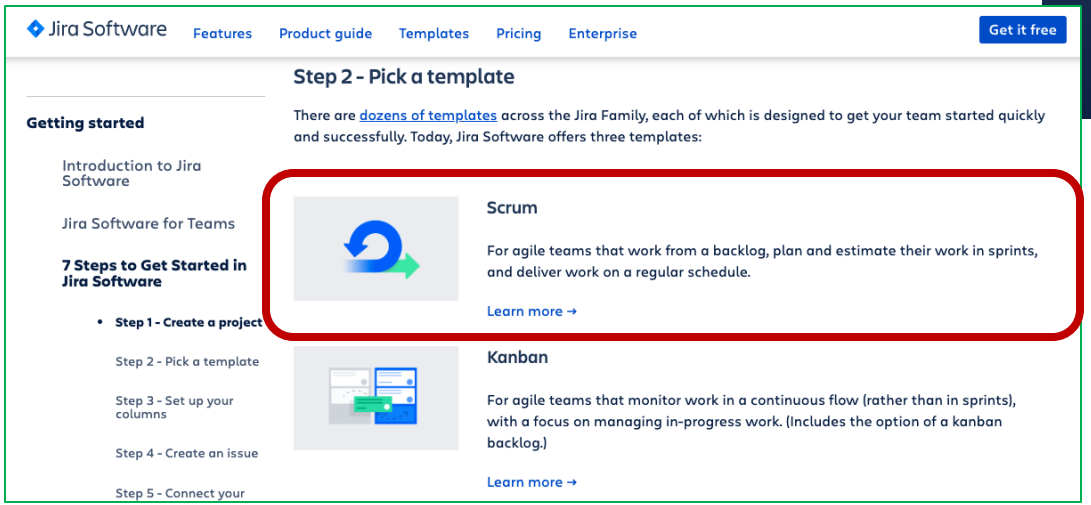

It's very important to select correct type of the project, as they have different structure.

Recap: What is the difference between Scrum and Kanban Jira boards/structures?

Standard Jira structure for Scrum:

Product backlog page

+

Board for the current sprint – created when you select items for a sprint and starts the sprint,
“To Do” == Sprint backlog

To Do	In Progress	In Review	Done

Standard Jira structure for Kanban:

Board for the whole project,
“To Do” == Product backlog

To Do	In Progress	In Review	Done

Jira: Extra videos/ reading materials

We shared with you in the Canvas module for this week (Week 6 - Lectorials and Workshops) additional learning material to help you with today's activities:

Video on Creating Scrum board in Jira (external video in YouTube, approx. 20 minutes)

Extra reading:

- Jira view on Scrum
- Jira Scrum Board

Activity 5: Discussion on Team-based assignment

In Week 5 Workshop we discussed Step 1 of this assessment.
Have you checked the Notes document?
Do you have any questions to the tutor?
Do you know your team?

Duration: approx. 20 minutes

Step 2: Based on your analysis of the above notes, create collaboratively the following artefacts:

- **Trello/Jira board, as it should be at the end of your Sprint 1 planning meeting:**
  - the board should present the product backlog, covering all points mentioned in the above notes (with correct priorities, story points, etc.),
  - all items (cards) that you selected for Sprint 1, should be moved to Sprint 1 backlog,
  - all items (cards) that you selected for Sprint 1, should have their sprint tasks and acceptance criteria specified,
- **Sprint Planning Notes for Sprint 1.**

Don't hesitate to ask tutor at the workshop if you have any questions.

Activity 6: Trello/Jira board – cards (external view, initial backlog)

Duration: approx. 15 minutes

Let's now start creating card on your Trello/Jira board for the A2 assignment scenario.

In this activity, you need to create **for this case study**:

- Cards with user stories as their names,
- Labels to present priorities and story points.

You have to work in your assignment team.
The tutor will make notes regarding your contributions to the team-work.

Note: We do not recommend using paid features of Trello/Jira, but if you decide to use them, please make sure that the corresponding elements are ready for marking till the end of the semester.

Activity 7: Trello/Jira board – cards (external view, Sprint 1 backlog)

Duration: approx. 10 minutes

Let's now select a set of cards for your Sprint 1 and move them to a Sprint backlog.

Discuss with the tutor your approach to select the tasks and the selected scope of the sprint.

Note: your expected velocity should be close to the ideal velocity.

You have to work in your assignment team.
The tutor will make notes regarding your contributions to the team-work.

Activity 8: Trello/Jira board – cards (internal view, sprint tasks)

Duration: approx. 15 minutes

Create sprint tasks for the cards you selected for the Sprint 1 backlog.

Note: In Trello, use two checklists – one for development tasks, another for QA tasks as per your DoD.

You have to work in your assignment team.
The tutor will make notes regarding your contributions to the team-work.
